

LEHI CITY


FIBER NETWORK MONTHLY UPDATE

September 25, 2024





LEHI FIBER TO MY CITY MAP

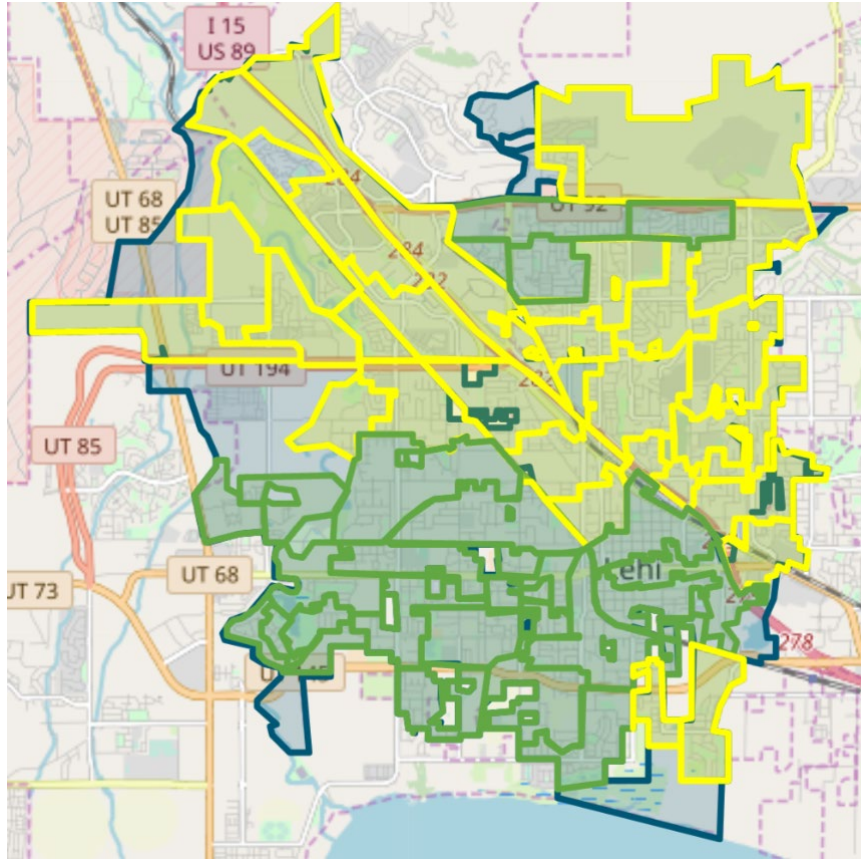

- Lehi City
- Construction in Progress
- Fiber Ready – Contact ISP

PROJECT OVERVIEW

NOTICE TO PROCEED

17 May 2022

DEMAND AGGREGATION LAUNCH

8 July 2022

GROUNDBREAKING CEREMONY

6 September 2022

SUBSTANTIAL COMPLETION

26 July 2025

COMPLETED BORING

175,863 feet


COMPLETED MICROTRENCHING

137,238 feet

COMPLETED FIBER PLACEMENT

883,026 feet

36-MONTH PROJECT TIMELINE

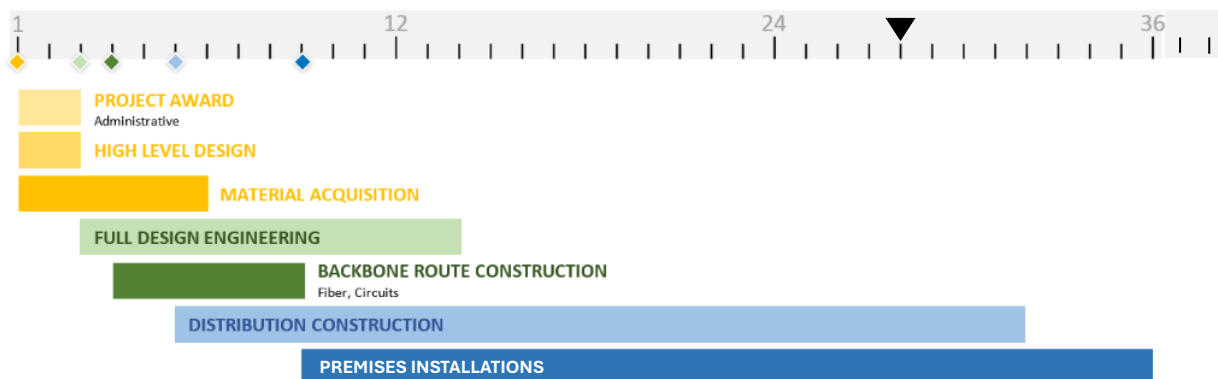



NETWORK OPERATIONS and NETWORK AREA CLOSE OUT

Strata Networks and Lehi City are working together to complete planning and fiber designs for Lehi Fiber facilities as part of new upcoming development projects that are within the city limits. Planning and care are provided so that these new developments can be integrated into the existing Lehi Fiber network systems under construction. Several of these new developments are under construction and others will begin construction within the upcoming weeks. When construction within a new development is completed, customers can sign up for services. A new development area, located within existing cabinet area 10A, has been completed such that customers may sign up for new services.

The Lehi Fiber team and Strata are working on construction punch lists, completion checklists, and details to complete and closeout some of the initial build cabinet and Network Areas. Once cabinet and Network Areas are fully complete and closed out, Lehi City will obtain ownership of those portions of the network. Customer sign ups and associated work that will occur after an area has been closed out will transition to network operations. The ability to sign up for service on the network does not change due to the close out and ownership transition of a network area to Lehi City. Once an area is opened for customer orders the sign-up process workflows and systems do not change.

ENGINEERING and CONSTRUCTION

RING AND DISTRIBUTION FIBER CONSTRUCTION

- Construction for **cabinets 37A, 36B, 19, 38, 40, 39, 41, 33, 32, 33N, 27A, 27B, 28A, 28B, 16A, 16B, 26, 14A, 14B, 20A, 24, 22, 20B, 6, and 29A** are in progress. Once construction is complete and fiber is placed, all locations within these cabinet boundaries may receive service. Notifications to the citizens informing them of service availability will be given at that time.
- Aerial make-ready work is continuing in **cabinets 14A and 14B**.
- Construction for additional cabinets will begin in the upcoming weeks.
- Initial communication with citizens generally occurs one week before cabinet areas begin construction.
- Construction for several cabinets are being completed. Fiber blowing and splicing has begun. These cabinets will be taking customer orders in the upcoming weeks. We are anticipating a cabinet being completed and ready for new customer orders about every other week.
- There are six total cabinet areas left to begin construction. Scheduling for remaining cabinets to start construction is being finalized.

Aerial make-ready work by Lehi Power is in progress for some of the cabinets under construction. Additional power make-ready work in other cabinet areas will begin in the upcoming weeks.

Joint use telecommunications make-ready work in all cabinet areas is intended to be completed during the Lehi Fiber aerial installation.



CUSTOMER INSTALLATIONS

Cabinet Areas 5, 18, 7, 9, 8, 4A, 4B, 10A, 10B, 17, 2, 13A, 13B, 3A, 3B, 21, 34, 37B, 35, 31, 30, and 11 are currently taking orders for new service. Customers within additional cabinet areas will be available once construction, fiber blowing, and fiber splicing are completed.

Coordination with the Lehi City team is ongoing to schedule and install fiber at city locations such as city parks, city buildings, power facilities, and water facilities. These locations are being installed once the construction in the serving cabinet area is complete and orders for new service connections are made available.



MARKETING/PUBLIC RELATIONS

DEMAND AGGREGATION

As of September 23, 2024, the demand aggregation platform reached a total of 9,744 unique addresses registered within city limits.

ADDITIONAL RESIDENT NOTIFICATIONS

Our team is actively exploring additional options to better communicate with residents about project updates.

LEHI FIBER OPEN HOUSE

On September 24, 2024, Lehi City hosted a fiber network open house where residents could come and learn more about the project, visit with ISPs, and enjoy a sweet treat. We were excited to help build assets for the event as well as have representatives from Strata in attendance.

TURN DOWN SURVEY EXPANSION

Our team is working closely with Lehi City to help gain better market intelligence on why residents may not be subscribing to the network. We plan to launch a broad campaign that includes emails and social media posts.
