


# FIBER NETWORK MONTHLY UPDATE

December 25, 2024





# **LEHI FIBER TO MY CITY MAP**

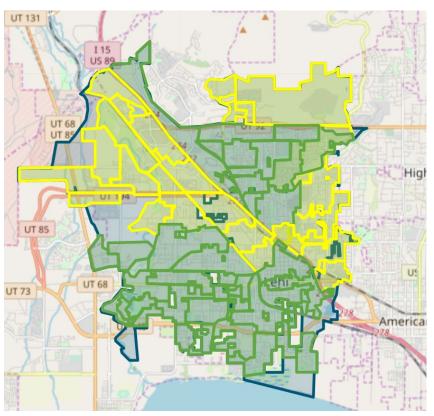

Lehi City

Construction in Progress

Fiber Ready – Contact ISP

## PROJECT OVERVIEW

**NOTICE TO PROCEED** 

17 May 2022

DEMAND AGGREGATION LAUNCH

8 July 2022

**GROUNDBREAKING CEREMONY** 

6 September 2022

SUBSTANTIAL COMPLETION

26 July 2025

**COMPLETED BORING** 

219,957 feet

**COMPLETED MICROTRENCHING** 

140,312 feet


COMPLETED FIBER PLACEMENT

2,057,732 feet

**EXISTING CONDUIT UTILIZED** 

605,725 feet

## **36-MONTH PROJECT TIMELINE**





## **NETWORK OPERATIONS and NETWORK AREA CLOSE OUT**

Strata Networks and Lehi City are working together to complete planning and fiber designs for Lehi Fiber facilities as part of new upcoming development projects that are within the city limits. Planning and care are provided so that these new developments can be integrated into the existing Lehi Fiber network systems under construction. When construction within a new development is completed, customers can sign up for services. New developments located within existing cabinet areas 10A, 17, and 35 have been completed, such that customers may sign up for new services.

The Lehi Fiber team and Strata are working on construction punch lists, completion checklists, and details to complete and closeout some of the cabinet and Network Areas. Once cabinet and Network Areas are fully complete and closed out, Lehi City will obtain ownership of those portions of the network. Customer sign ups and associated work that will occur after an area has been closed out will transition to network operations. The ability to sign up for service on the network does not change due to the close out and ownership transition of a network area to Lehi City. Once an area is opened for customer orders the sign-up process workflows and systems do not change.

### **ENGINEERING and CONSTRUCTION**

#### RING AND DISTRIBUTION FIBER CONSTRUCTION

- Construction for cabinets 40, 33N, 27A, 27B, 28A, 28B, 16A, 16B, 26, 14B, 20A, 24, 22, 20B, 6, 29A, 29B, 12 and 42 are in progress. Once construction is complete and fiber is placed, all locations within these cabinet boundaries may receive service. Notifications to the citizens informing them of service availability will be given at that time.
- Aerial make-ready work for cabinet 22 is being finalized.
- Construction for several cabinets is being completed. Fiber blowing and splicing has begun. These cabinets will be taking customer orders in the upcoming weeks. We are anticipating a cabinet being completed and ready for new customer orders about every week through the first two months of the new year.
- There are five total cabinet areas left to begin construction. Construction for the remaining cabinet areas will begin throughout January and February 2025.
- Initial communication with citizens generally occurs one week before cabinet areas begin construction.

Aerial make-ready work by Lehi Power is in progress for some of the cabinets under construction. Cabinet 22 is the last remaining cabinet where make-ready work is needed.

Joint use telecommunications make-ready work in all cabinet areas is intended to be completed during the Lehi Fiber aerial installation.

#### **CUSTOMER INSTALLATIONS**

Cabinet Areas 5, 18, 7, 9, 8, 4A, 4B, 10A, 10B, 17, 2, 13A, 13B, 3A, 3B, 21, 34, 37B, 35, 31, 30, 11, 1B, 38, 39, 37A, 1A, 36A, 36B, and 32 are currently taking orders for new service. Customers within additional cabinet areas will be available once construction, fiber blowing, and fiber splicing are completed.



City locations are being installed once construction in the serving cabinet area is complete and orders for new service connections are made available.

## MARKETING/PUBLIC RELATIONS

#### **DEMAND AGGREGATION**

As of December 15, 2024, the demand aggregation platform reached a total of **10,014** unique addresses registered within city limits.

#### **VALUE OF FIBER**

Recently, we gathered additional market insights as to why some residents haven't switched to the Lehi Fiber Network. In response, the Strata marketing team is working closely with Lehi City to develop a campaign promoting the value of a fiber internet connection. We hope to address residents' concerns while explaining the value of a fiber internet connection.
